Scope of Work: CITT Workplan for Water Measurement at Instream Flow, River Diversion Allowance, Natural Flow and Irrigation Return Flow Locations

Approved May 24, 2016

Table of Contents

1.0	Executive Summary	. 2
2.0	Water Measurement as it relates to the Compact	.3
3.0	Background and Existing CSKT Water Management Program	. 4
4.0	Proposed Additions to the Water Measurement Program	. 6
5.0	Budget	11
6.0	Schedule	15
Supple	ment 1.0: Existing CSKT Water Measurement Program	
Supple	ment 2.0: Proposed CSKT Water Measurement Program Expansion	

List of Abbreviations

CSKT Confederated Salish and Kootenai Tribes CITT **Compact Implementation Technical Team** FIIP Flathead Indian Irrigation Project Interim Instream Flow IIF ISF Instream Flow Montana Bureau of Mines and Geology **MBMG** MEF Minimum Enforceable Instream Flow TIF Target Instream Flow RDA **River Diversion Allowance** USGS **United States Geological Survey**

1.0 Executive Summary

The Confederated Salish and Kootenai Tribes (CSKT) – Montana Water Rights Compact (Compact) identifies stream and canal locations where water measurement will be needed to effectively allocate water between instream flow and irrigation demands. The Compact also sets forth the Compact Implementation Technical Team (CITT) and charges them, during the current pre-Effective Date period, with making technical recommendations for expanding the existing CSKT Water Measurement Program (Program) in a manner that instream flow (ISF) and river diversion allowance (RDA) measurement requirements are met. Recommendations in this proposal are prepared for the parties to the Compact to consider.

The body of this proposal provides background and detail, including the schedule and budget. Supplement One describes the existing CSKT Water Measurement Program, and Supplement Two describes the proposed expansion to the CSKT Water Measurement Program. The proposal assumes some familiarity with terminology found in the Compact. For readers needing clarification, the definitions section of the Compact found at http://dnrc.mt.gov/divisions/reserved-water-rights-compact-commission/confederated-salish-and-kootenai-tribes defines specific terms.

This proposal recommends flow measurement at locations where instream flows will be enforced, locations where natural flow will be monitored for predicting water availability, and flow measurement at RDA canal and irrigation return flow locations. Measurement locations are planned-for in Section 3.d. of Appendix 3.5 to the Compact. Specifically, the CITT recommends:

- a. Installation of one new ISF station;
- b. Installation of 17 new RDA stations;
- c. Upgrades to six currently operated ISF stations;
- d. Upgrades to four currently operated RDA stations;
- e. Development of a monitoring protocol at 11 ISF sites and eight RDA stations;
- f. Upgrades to two natural flow measurement locations;
- g. New installations at three irrigation return flow locations; and
- h. Placement of artificial control sections at sixteen canal locations.

With implementation of this proposal, the existing CSKT Water Measurement Program will be expanded to address all Compact-related measurement requirements at ISF and RDA locations. Additionally, the

CITT will work together with the CSKT Water Measurement Program to achieve implementation and ensure implementation effectiveness.

This recommendation is contingent upon the following principles:

- The CSKT Water Measurement Program will continue to function as the principal entity with regards to water measurement at existing CSKT locations and locations added through this proposal;
- 2. Existing and future flow data will be processed and made accessible to the public via internet, and archived and managed by the CSKT;
- Funding is available annually for the full ten-year period identified in the proposal;
- 4. As approved by the CITT, detailed site-assessments may justify modification of equipment and station placement outlined in this proposal; and
- 5. A cooperative status be maintained between the CSKT Water Measurement Program and the CITT.

The total cost for the ten-year proposal is \$1,428,088, with \$375,847 being allocated during the first year. A detailed annualized budget is included in Section 5.0, with an implementation schedule included in Section 6.0.

The CITT encourages the parties to the Compact to support and fund this proposal for expanding and enhancing the existing CSKT Water Measurement Program to include the locations set forth by the Compact. This action will improve the ability to implement operational improvements and simultaneously achieve ISF and irrigation demand (RDA) targets following the Effective Date and implementation of the Compact.

2.0 Water Measurement as it relates to the Compact

Water measurement, data management/dissemination, and planning for and allocation of water between instream and irrigation uses of water are explicitly called for in the Compact and Appendices 3.1 through 3.7 to the Compact. This occurs in part because:

- MEF, TIF and RDA levels are set to vary based on defined wet through dry water-year types;
- MEF and TIF levels are set to be incrementally met as operational improvements occur on the FIIP;

- Seasonal water supply planning and potential within-season adjustments to water allocations are keyed to water measurement information;
- Shared shortage conditions are identified based on water measurement information;
- Compliance for Interim Instream Flows (IIFs) have relied on measurement since the late 1980's, and will continue to for a period of time; and
- The FIIP water use right is satisfied and tracked through measurement at RDA locations.

Specifically, Articles IV. C., D., and E. of the Compact recognize the role of water measurement and Article IV. F. confirms this, explicitly identifying comprehensive water measurement as essential to the Compact. Appendices 3.1 through 3.7 call for water measurement, with Appendix 3.4 identifying water measurement in the operational improvements schedule, and Appendix 3.7 identifying indicator natural flow stream gages for determination of wet through dry years. In Appendix 3.5, the guidance document for CITT activities, water measurement is identified as a task in several locations, and Section 3.d.i. identifies that the Tribes shall manage data at instream flow, RDA, and irrigation return flow locations.

Water measurement has been, and will continue to be, critical on streams and canals associated with the FIIP due to the variability in seasonal runoff volumes, the complexity of the stream and canal network, and the very high level of utilization of available water supply for irrigation uses.

3.0 Background and Existing CSKT Water Management Program

This proposal builds on the CSKT Water Management Program (Program) gaging network and program capabilities. The CSKT Water Measurement Program has been active since 1982. The Program currently has four full-time hydro-technicians, a data management hydrologist, and a supervisory hydrologist. Currently the Tribes commit approximately 450,000 dollars annually toward the existing water measurement program, an effort that has served to provide substantial information used for purposes of FIIP operations, interim ISF management, and Compact negotiations. Most of the Compact-related ISF stations are part of the current Tribal measurement network, and a large number of Compact-related RDA stations are part of the current Tribal network or were historically part of the network.

Emphasis has historically been placed on surface water measurement; however the Program also maintains a groundwater monitoring network. The Program completes monitoring for the Tribes' Safety of Dams program, and the Program completes water quality monitoring and special projects work. Since

approximately 1990, the Program has participated in the NRCS snow survey program, and is currently one of the largest cooperators in the State, monitoring snowpack from Marias Pass south to the Rattlesnake Range.

Also since 1982, the Program has maintained cooperator status with the Montana US. Geological Survey office. Several activities have occurred through the cooperator arrangement, including larger water resource studies, extensive training and quality assurance for Program staff, and maintenance of a set of natural flow stream gages on the Reservation. Starting in 1992, as the Program transitioned to greater use of continuously recording equipment, the USGS completed site evaluations and installation recommendations for measurement stations, many of which are still operational. For a period of six years, the Program employed a retired USGS hydro-technician full-time to work with Tribal staff on field and data management techniques.

Field and office procedures rigorously adhere to standard operating procedures prepared by the Program and procedures found in various USGS publications (ex: USGS WSP 2175, 1982; USGS TM 3-A8, 2010; USGS TM 3-A22, 2013). Gaging station data and rating curves are compiled by field staff, reviewed and quality assured by the chief of field operations, and finally quality assured by a hydrologist. Data are currently maintained in an SQL database developed for the Program; this database houses all records dating back to 1982, including records for over 100 active or discontinued stream stations, over 70 active or discontinued canal stations, and 21 active or discontinued irrigation return flow stations. Hard copy data management files are also maintained and hold annual station analyses, level notes, rating curves and other station details.

In the last three years, the Program has completed the following upgrades.

- Field staff have discontinued use of mechanical stream gaging meters and use acoustic doppler velocimeters (ADV's) for wading discharge measurements.
- Field staff use an acoustic doppler current profiler (ADCV) for peak flow and large canal measurements.
- Electronics at forty five stations have been upgraded to support telemetry and real-time data
 acquisition using the GOES satellite network for data transmission. These data are reported to a
 dedicated website.
- The Program is currently transitioning from their SQL database to the Aquatic Informatics Aquarius
 Time Series database and Aquarius Web data portal. This data management software has been selected by the USGS and Water Resource Survey of Canada as their primary data management

platform, and will provide a robust data management solution for the Water Management Program. The database transition is ongoing with completion expected in mid to late 2016.

• The Program is scanning hard copy records prior to 2015 for electronic data storage and retrieval.

Currently, the Program maintains 66 active stations – 38 stream stations, 25 canal stations, and three irrigation return flow stations. Twenty of the stream stations are identified as ISF compliance locations in the Compact and twenty of the canal stations are identified as RDA stations in the Compact. Three return flow stations are monitored to assist FIIP comply with the biological opinion for project operations.

The cost savings that will accrue to CITT-related water measurement responsibilities from the existing Tribal investment in water measurement are significant and include:

- Numerous active stream and canal stations with greater than a 20-year period of quality-assured and fully documented record. This dataset provides insight into streamflow variability, streamflow trends, and ISF and FIIP operations under various water supply scenarios;
- Forty instream flow and RDA compliance locations, most of which are equipped for telemetry;
- Investment in a database and web-based reporting system;
- A fully operational and equipped program with expertise developed over 34 years; and
- A program that is able to incorporate new responsibilities and train new staff.

Supplement One includes: a) maps and tables showing the existing stream, canal, and return flow monitoring network; and b) a position description for the Water Management Program hydro-technician job.

4.0 Proposed Additions to the Water Measurement Program

Proposed additions to the measurement program to support CITT activities focus on ISF and RDA locations, but also include natural flow locations which are part of the definition of wet through dry water-year types, and additional irrigation return flows. Focus for ISF and RDA locations is to bring these stations forward to support telemetry and real-time data acquisition.

There are a number of instream flow and RDA stations where a monitoring protocol is recommended, instead of the investment in a continuously recording station and the associated long-term operations cost. These situations occur where the specified flow levels are low or the canal headworks water management does not require system-level coordination. The primary monitoring protocol will be to

identify a measurement section, install a staff gage, and complete check measurements and maintain a rating, as needed. Experience will indicate which stations require more diligence for measurement and rating work. The Flathead River pumping plant is a unique situation because the pump canal is a level canal supporting two-way flow. Pump volume records will be maintained by tracking electrical usage and on-off times for the pumps. This will require preparation of a standard operating procedure for information reporting.

Irrigation return flow stations are identified for measurement in the Compact. While there are well over 30 active return flow locations on the FIIP, the CITT recommends maintaining three currently operating return flow stations and adding three return flow locations which have been shown to carry higher flow volumes.

Natural streamflow information is needed for water supply forecasting and to define wet through dry water-year conditions. The proposal identifies upgrades to two existing CSKT stations which are applied for water-year definitions. USGS natural flow stations are maintained through the CSKT-USGS cooperative agreement. The Tribes and the CITT recognizes that this program is challenging to fund, and may need to look to alternative funding sources in future years.

Some premises for proposed additions to the measurement program follow:

- All continuous monitoring stations should support telemetry;
- All telemetered data should be available to the public via website access;
- Artificial controls (weirs or flumes, other) should be placed in canals to reduce long-term operational
 costs;
- A monitoring protocol should be applied where continuous monitoring may not be warranted; and

Access to data will occur through the Aquarius Web portal, which will be identified on the CITT website and accessible to the general public. The CITT is also exploring options to provide access to data through the Montana Bureau of Mines and Geology surface water web data portal. The CITT supports this concept, and is working with the MBMG to evaluate options. Costs that may be associated with MBMG data hosting are not reflected in this proposal.

Supplement Two contains equipment details and several tables that break-out measurement stations by proposed activities; these tables form the basis for the budget. Table 1.0 below sequentially summarizes measurement plans for MEF and TIF locations, as they are found in Appendix 3.1 to the Compact. Table 2.0 sequentially summarizes measurement plans for RDA locations, as they are found in Appendix 3.2 to

the Compact. Table 3.0 summarizes natural flow and irrigation return flow locations proposed for measurement activity. Table 4.0 identifies the initial priority list for installation of artificial controls in canal sections. Table S2.d (Supplement 2) contains the full list of canals identified for artificial controls.

Table 1.0: Measurement activities at MEF and TIF locations

Orange – existing CSKT telemetry station and equipment, count = 14;

Green – existing CSKT station with proposed upgrade to monitoring equipment, count = 6;

Yellow – new installation, count = 1;

Station name	Station type	Measurement plan	Notes
Middle Fork Jocko River	IIF/MEF/TIF	Existing equipment	
North Fork Jocko River	IIF/ MEF/TIF	Existing equipment	
Falls Creek below Tabor Feeder	MEF/TIF	Monitoring protocol	Install staff gage or rate orifice gate planned for 2016 construction
S-14 Creek below Tabor Feeder	MEF/TIF	Monitoring protocol	Install staff gage after gate reconstructed in Tabor Feeder Canal
Jocko River below Upper S Canal	IIF/ MEF/TIF	Monitoring protocol	Maintain staff gage and rating, use downstream river gage at K Canal for primary water management
Cold Creek below Upper S Canal	MEF	Monitoring protocol	Install staff gage after gate reconstructed in Upper S Canal
Gold Creek below Upper S Canal	MEF	Monitoring protocol	Install staff gage after gate reconstructed in Upper S Canal
Big Knife Creek below Upper S Canal	IIF/MEF/TIF	Upgrade to telemetry	
Jocko River at K Canal	IIF/MEF/TIF	Existing equipment	
Agency Creek below Upper J Canal	IIF/MEF/TIF	Upgrade to telemetry	
East Fork Finley Creek below N	IIF/MEF/TIF	Upgrade to telemetry	
Schley Creek below Doney Ditch	MEF/TIF	Monitoring protocol	Install staff gage
Finley Creek near mouth	IIF/MEF/TIF	Existing equipment	
Jocko River below lower S Canal	IIF/MEF/TIF	Upgrade to telemetry	
Jocko River below lower J Canal	IIF/MEF/TIF	Existing equipment	
Revais Creek below Revais R	MEF/TIF	New installation	
Mission Creek below Pablo Feeder Canal	IIF/MEF/TIF	Existing equipment	
Post Creek above Pablo Feeder Canal	MEF/TIF	Existing equipment	
Middle Crow Creek below Pablo Feeder Canal	IIF/MEF/TIF	Upgrade to telemetry	
North Crow Creek below Pablo Feeder Canal	IIF/MEF/TIF	Existing equipment	
Mission Creek below 6C Canal	IIF/MEF/TIF	Existing equipment	Station moved to St. Ignatius due to poor measuring conditions around HW 93
Post Creek below F Canal	IIF/MEF/TIF	Existing equipment	
Marsh Creek below KH Feeder	IIF/MEF/TIF	Monitoring protocol	Use existing staff gage and measurement location
South Crow Creek below South Crow Feeder	IIF/MEF/TIF	Existing equipment	
Crow Creek below Crow Pump	IIF/MEF/TIF	Existing equipment	
Mud Creek below Ronan B Canal	IIF/MEF/TIF	Upgrade to telemetry	
Crow Creek below Moiese A Canal	IIF/MEF/TIF	Existing equipment	

Station name	Station type	Measurement plan	Notes
Hellroaring Creek below Twin	MEF	Monitoring protocol	Install staff gage
Feeder Canal			
Little Bitterroot River above Mill	MEF	Monitoring protocol	Install staff gage
Creek			
Mill Creek below Camas A Canal	MEF	Monitoring protocol	Install staff gage
Little Bitterroot River below Mill	IIF/MEF/TIF	Existing equipment	
Creek			
Hot Springs Creek below Camas	IIF / MEF	Monitoring protocol	Install staff gage
C Canal			
Little Bitterroot River below Hot			No action
Springs Creek			

Table 2.0: Measurement activities at RDA locations

Orange – existing CSKT station and equipment, count = 16;

Green – existing CSKT station with proposed upgrade to monitoring equipment, count = 4;

Yellow – new installation, count = 17;

Grey – monitoring protocol, count = 8

Station name	Station type	Measurement plan	Notes
Tabor Feeder Canal below MF Jocko River	RDA	Upgrade to telemetry	
Tabor Feeder Canal below NF Jocko River	RDA	Existing equipment	
Tabor Feeder Canal below Twin Lakes	RDA	Existing equipment	
Placid Canal above Black Lake	Incremental inflow	Existing equipment	
Upper Jocko S Canal at headworks at Jocko River	RDA	Existing equipment	
Upper Jocko S Canal at Big Knife Creek	RDA	New installation	
Jocko K Canal at headworks	RDA	Existing equipment	
Upper Jocko S Canal at Agency Creek	RDA	New installation	
Upper Jocko J Canal at Agency Creek	RDA	New installation	
Jocko E Canal at Agency Creek	RDA	New installation	
Jocko E Canal below Finley Creek	RDA	New installation	
Jocko N Canal at East Fork Finley Creek	RDA	New installation	
Doney Ditch at Schley Creek	RDA	Monitoring protocol	Install staff gage
Lower Jocko S Canal at Jocko River	RDA	New installation	
Lower Jocko J Canal at Jocko River	RDA	New installation	
Revais R Canal at Revais Creek	RDA	New installation	
Mission DA Canal at DC pool	RDA	Upgrade to telemetry	
Mission A Canal below Mission Creek	RDA	Existing equipment	
Pablo Feeder Canal below Post Creek	RDA	Existing equipment	
Pablo Feeder Canal below South Crow Creek	RDA	New installation	

Station name	Station type	Measurement plan	Notes
Pablo Feeder Canal below	RDA	Monitoring protocol	Install staff gage
Middle Crow Creek			
Pablo Feeder Canal below North	RDA	Existing equipment	
Crow Creek			
Pablo Feeder Canal at Pablo	RDA	Existing equipment	
Drop			
DC-2 Lateral at Dry Creek lining	RDA	Monitoring protocol	Install staff gage
Cold Creek Ditch at Cold Creek	RDA	Monitoring protocol	Install staff gage
Mission F Canal at headworks	RDA	Upgrade to telemetry	
Mission B Canal at Mission Creek	RDA	New installation	
Mission C Canal at Mission	RDA	Existing equipment	
Creek	NDA	Existing equipment	
Mission 6C Canal at Mission	RDA	New installation	
Creek	ND/	New instanction	
Kicking Horse Feeder at Post	RDA	Existing equipment	
Creek		zwern8 edarbment	
Post F Canal at Post Creek	RDA	Existing equipment	
Mission H Canal at Mission	RDA	New installation	
Creek			
South Crow Feeder at South	RDA	Upgrade to telemetry	
Crow creek			
Crow Pump Canal at Crow Creek	RDA	Monitoring protocol	Install staff gage
Ronan B Canal at Mud Creek	RDA	New installation	
Moiese A Canal at Crow Creek	RDA	Existing equipment	
Hillside Ditch	RDA	Existing equipment	
Twin Feeder Canal at Hellroaring	RDA	Monitoring protocol	Install staff gage
Creek			
Twin Feeder Canal at Centipede	RDA	New installation	
Creek			
Lower Twin Feeder Canal at	RDA	Monitoring protocol	Install staff gage
Bisson Creek	DDA	Fuinting and income	
Pablo A Canal below Pablo Reservoir	RDA	Existing equipment	
Flathead River Pumping Plant	RDA	Monitoring protocol	Derive flow from power usage
Camas A Canal at Mill Creek	RDA	Existing equipment	1 1 1 1 1 1 1 1
McGinnis Diversion	RDA	New installation	
Alder Diversion	RDA	New installation	

Table 3.0: Measurement activities at Natural Flow and Irrigation Return Flow locations
Orange – existing CSKT/USGS station and equipment, count = 7;
Green – existing CSKT station with proposed upgrade to monitoring equipment, count = 2;
Yellow – new installation, count = 3

Station name	Station type	Measurement plan	Notes
South Fork Jocko River	Natural flow	Existing USGS coop	Part of definition for wet/dry/normal years
Agency Creek above Upper S Canal	Natural flow	Upgrade to telemetry	Part of definition for wet/dry/normal years
South Crow Creek	Natural flow	Existing USGS coop	Part of definition for wet/dry/normal years
North Crow Creek	Natural flow	Upgrade to telemetry	Part of definition for wet/dry/normal years
Hellroaring Creek	Natural flow	Existing CSKT station	Part of definition for wet/dry/normal years
Mill Creek	Natural flow	Existing USGS coop	Part of definition for wet/dry/normal years
Dublin Gulch	Return flow	Existing equipment	BIOP compliance
Coleman Coulee	Return flow	Existing equipment	BIOP compliance
Moiese MA Canal	Return flow	Existing equipment	BIOP compliance
West Miller Coulee	Return flow	New installation	Large return flow to Mud Creek from Pablo area
Hopkins Draw	Return flow	New installation	Large return flow to Flathead River from Round Butte
Westphal Coulee	Return flow	New installation	Large return flow to Flathead River from Valley View

Table 4.0: Initial priorities for artificial controls in canals. Further prioritization will be based on experience installing initial structures

Station	Priority ranking	Planned-for control structure
Hillside Ditch	1	Flume
Mission B Canal	2	Flume
Lower Jocko J Canal	3	Flume
Lower Jocko S Canal	4	Flume

5.0 Budget

The budget estimate for the proposed work is broken into one of four categories: CSKT staffing costs; equipment costs; database costs; and artificial control structure costs.

- CSKT staff costs are based on a ten year term. Planning for water measurement activities cannot
 effectively proceed on a one year term and CSKT staff costs are not provided on this basis. Staff
 costs include:
 - One full-time hydro-technician progressing from hydro-technician level 1 to level 2 after two
 years. This position is essential considering the increased number of measurement stations.
 Support costs, including vehicle and one-time purchase of field equipment are included.

- Part-time FTE's (0.20 FTE) for the data management hydrologist and chief of field operations. These positions are intimately involved in all aspect of Water Management Program work, and are essential for effective implementation of proposed work.
- Equipment costs include costs for installation of new stations, upgrades to existing stations, and staff gage installations. Installation field service costs (equipment and operator, labor) are included.
 An electronics maintenance budget is based on Program experience that certain of the electronics equipment requires maintenance, repair or replacement during and after the warranty period.
- Database costs are directly attributable to costs to increase the number of stations reporting to Aquarius Web.
- Artificial control structure costs are based on installation of 16 structures. Costs for structures are included in the ten-year projections.

Table 5.0: Budget Compilation

Item	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9	Year 10	Totals
<u>Labor</u>		_						_			
1.0 fte hydro-tech	\$46,678	\$48,078	\$50,000	\$51,500	\$53,045	\$54,636	\$56,275	\$57,964	\$59,703	\$61,494	\$539,37
0.2 fte data hydrologist	\$14,056	\$14,477	\$14,912	\$15,359	\$15,820	\$16,294	\$16,783	\$17,278	\$17,805	\$18,339	\$161,13
0.2 fte chief of field operations	\$15,547	\$16,014			Resp	onsibilities dec	rease after insta	allation			\$31,561
CSKT indirect	\$16,019	\$16,500	\$13,631	\$14,040	\$14,462	\$14,895	\$15,342	\$15,803	\$16,277	\$16,765	\$153,73
										Labor Subtotal	\$885,79
Hydro-tech field support											
Vehicle	\$7,230	\$7,375	\$7,522	\$7,673	\$7,826	\$7,983	\$8,142	\$8,305	\$8,471	\$8,641	\$79,166
Equipment start-up	\$15,000										\$15,000
	<u> </u>	<u> </u>			_				Field Su	pport Subtotal	\$94,166
Database costs											
Increase # of web portal locations	\$6,000										\$6,000
Support and maintenance add-ons	\$1,500	\$1,200	\$900	\$900	\$1,500	\$1,500	\$1,500	\$1,500	\$1,500	\$1,500	\$13,500
									Dat	abase Subtotal	\$19,500
Station Electronics											
Satlink V2	\$2,516										\$83,028
GOES antenna	\$314										\$10,362
lightning protector	\$144										\$4,752
lightning protector SD1-12 Shaft Encoder	\$144 \$738										\$4,752 \$24,354
SD1-12 Shaft Encoder cable assembly 15ft.	\$738										\$24,354
SD1-12 Shaft Encoder	\$738 \$125										\$24,354 \$4,125
SD1-12 Shaft Encoder cable assembly 15ft. float wheel	\$738 \$125 \$224										\$24,354 \$4,125 \$7,392
SD1-12 Shaft Encoder cable assembly 15ft. float wheel graduated float tape	\$738 \$125 \$224 \$179										\$24,354 \$4,125 \$7,392 \$5,907
sD1-12 Shaft Encoder cable assembly 15ft. float wheel graduated float tape counterweight and endhook 20 watt solar panel	\$738 \$125 \$224 \$179 \$64										\$24,354 \$4,125 \$7,392 \$5,907 \$2,112
sD1-12 Shaft Encoder cable assembly 15ft. float wheel graduated float tape counterweight and endhook 20 watt solar panel 4 amp solar panel charger	\$738 \$125 \$224 \$179 \$64 \$369										\$24,354 \$4,125 \$7,392 \$5,907 \$2,112 \$12,177
SD1-12 Shaft Encoder cable assembly 15ft. float wheel graduated float tape counterweight and endhook	\$738 \$125 \$224 \$179 \$64 \$369 \$89										\$24,354 \$4,125 \$7,392 \$5,907 \$2,112 \$12,177 \$2,937

Site hardware	\$400										\$13,200
Per station total	\$5,753		•	•			•	Elec	tronics subtota	l (33 stations)	\$ 189,849
Electronics maintenance			\$15,188				\$ 15,188				\$ 30,868
		<u>I</u>	<u> </u>	•			<u> </u>	Elec	tronic mainten	ance subtotal	\$ 30,868
Station housing											L
Staff gage, channel iron	\$340										\$7,140
Steel equip. shelters	\$775										\$16,275
24", 16 gage 8' cmp	\$198										\$4,158
Cmp base plates, welding	\$195										\$4,095
Site hardware	\$200										\$4,200
	1	1	ı	1	l	l	1	Station h	ousing subtota	l (21 stations)	\$35,868
Installation –field services	\$9,800										\$ 9,800
		1		<u> </u>			<u> </u>	<u> </u>	Install	ation subtotal	\$ 9,800
									mstan	ation subtotal	¥ 3,000
				Total	without Artificia	al Controls			mstan	ation subtotal	7 3,000
	357,547	\$103,643	\$102,153	Total v \$89,472	without Artificia	\$95,309	\$113,231	\$100,858	\$103,756	\$106,739	\$1,265,359
Artificial Controls	357,547 2 sites	\$103,643 2 sites	\$102,153 2 sites				\$113,231 2 sites	\$100,858 2 sites			
CIP concrete (\$ 700.00			<u> </u>	\$89,472	\$92,652	\$95,309		<u> </u>			
CIP concrete (\$ 700.00 cuyard)	2 sites	2 sites	2 sites	\$89,472 2 sites	\$92,652 2 sites	\$95,309 2 sites	2 sites	2 sites			\$1,265,359
CIP concrete (\$ 700.00 cuyard) bedding material	2 sites \$16,800	2 sites \$17,304	2 sites \$17,823	\$89,472 2 sites \$18,358	\$92,652 2 sites \$18,909	\$95,309 2 sites \$19,476	2 sites \$20,060	2 sites \$20,662			\$1,265,359 \$149,391
CIP concrete (\$ 700.00 cuyard) bedding material	2 sites \$16,800 \$1,000	2 sites \$17,304 \$1,030	2 sites \$17,823 \$1,061	\$89,472 2 sites \$18,358 \$1,093	\$92,652 2 sites \$18,909 \$1,126	\$95,309 2 sites \$19,476 \$1,159	2 sites \$20,060 \$1,194	2 sites \$20,662 \$1,230		\$106,739	\$1,265,359 \$149,391 \$8,892
Artificial Controls CIP concrete (\$ 700.00 cuyard) bedding material misc. CSKT design, surveying [CSKT in kind]	2 sites \$16,800 \$1,000	2 sites \$17,304 \$1,030	2 sites \$17,823 \$1,061	\$89,472 2 sites \$18,358 \$1,093	\$92,652 2 sites \$18,909 \$1,126	\$95,309 2 sites \$19,476 \$1,159	2 sites \$20,060 \$1,194	2 sites \$20,662 \$1,230	\$103,756	\$106,739	\$1,265,355 \$149,391 \$8,892 \$4,446
CIP concrete (\$ 700.00 cuyard) bedding material misc.	2 sites \$16,800 \$1,000 \$500	2 sites \$17,304 \$1,030 \$515	2 sites \$17,823 \$1,061 \$530	\$89,472 2 sites \$18,358 \$1,093 \$546	\$92,652 2 sites \$18,909 \$1,126 \$563	\$95,309 2 sites \$19,476 \$1,159 \$580	2 sites \$20,060 \$1,194 \$597	2 sites \$20,662 \$1,230 \$615	\$103,756	\$106,739	\$1,265,359 \$149,391 \$8,892 \$4,446 \$162,730
CIP concrete (\$ 700.00 cuyard) bedding material misc. CSKT design, surveying [CSKT in kind]	2 sites \$16,800 \$1,000 \$500 \$4,000	2 sites \$17,304 \$1,030 \$515 \$4,120	2 sites \$17,823 \$1,061 \$530 \$4,244	\$89,472 2 sites \$18,358 \$1,093 \$546	\$92,652 2 sites \$18,909 \$1,126 \$563 \$4,502	\$95,309 2 sites \$19,476 \$1,159 \$580 \$4,637	2 sites \$20,060 \$1,194 \$597 \$4,776	2 sites \$20,662 \$1,230 \$615 \$4,920	\$103,756 Subtotal dir	\$106,739	\$1,265,359 \$149,391 \$8,892 \$4,446 \$162,730 \$35,569
CIP concrete (\$ 700.00 cuyard) bedding material misc. CSKT design, surveying [CSKT in kind]	2 sites \$16,800 \$1,000 \$500 \$4,000	2 sites \$17,304 \$1,030 \$515 \$4,120	2 sites \$17,823 \$1,061 \$530 \$4,244	\$89,472 2 sites \$18,358 \$1,093 \$546	\$92,652 2 sites \$18,909 \$1,126 \$563 \$4,502	\$95,309 2 sites \$19,476 \$1,159 \$580 \$4,637	2 sites \$20,060 \$1,194 \$597 \$4,776	2 sites \$20,662 \$1,230 \$615 \$4,920 \$6,149	\$103,756 Subtotal dir	\$106,739 ect costs I in kind costs	\$1,265,359 \$149,391 \$8,892 \$4,446 \$162,730 \$35,569 \$44,462
CIP concrete (\$ 700.00 cuyard) bedding material misc. CSKT design, surveying [CSKT in kind]	2 sites \$16,800 \$1,000 \$500 \$4,000	2 sites \$17,304 \$1,030 \$515 \$4,120	2 sites \$17,823 \$1,061 \$530 \$4,244	\$89,472 2 sites \$18,358 \$1,093 \$546	\$92,652 2 sites \$18,909 \$1,126 \$563 \$4,502	\$95,309 2 sites \$19,476 \$1,159 \$580 \$4,637	2 sites \$20,060 \$1,194 \$597 \$4,776	2 sites \$20,662 \$1,230 \$615 \$4,920 \$6,149	\$103,756 Subtotal dir	\$106,739 ect costs I in kind costs	\$1,265,359 \$149,391 \$8,892 \$4,446 \$162,730 \$35,569 \$44,462 \$80,031

6.0 Schedule

The schedule for project implementation is contingent based on approval of the proposal and disbursement of funds to implement the proposal. Consequently, the schedule is defined in terms of time following funds disbursement. However, the schedule may need to be modified based on timing of funds disbursement, as it relates to irrigation activities and canal access and seasonal weather that may affect construction.

Hillside Ditch and Mission B Canal are identified for installation of a ratable, artificial control in fall, 2016. Lower Jocko J Canal and Lower Jocko S Canal are identified for installation of a ratable, artificial control in spring, 2017. These dates could change, pending project start-up.

Table 6.0: Schedule

Acti	vity	Time following funds disbursement
1	Hire field hydrographer	3 months
2	Adapt workloads for Data Hydrologist and Chief of Field	3 months
	Operations	
3	Purchase and receipt of gage station electronics	4 months
4	Purchase, fabrication, and receipt of gage station wet wells and	6 months
	gage houses	
5	Upgrade gaging equipment at existing stations	6 months
6	Install wet wells, gage houses and gage station electronics at new	8 months
	stations	
7	Install staff gages at monitoring protocol stations	12 months
8	Database activities, including new GOES assignments	4 months
9	Install control structures	2 – fall 2016, 2 – spring 2017

Supplement One: Existing Tribal Water Measurement Program

This supplement contains: a) maps and tables with currently active CSKT Water Management Program gaging stations; and b) a position description for the Program hydro-technician position. This is included to illustrate the job responsibilities for the staff position identified in the project budget. This position description has been used for recent hires.


Table S.1a: Active CSKT/USGS stream gages [IIF = interim instream flow location; MEF and TIF = Compact instream flow location; stream = active station that is not a proposed instream flow compliance station]

Station Identifier	Station Name	Station Type	Period of Record
500000	Placid Creek below Placid Canal	IIF	1989 - P
510000	Middle Fork Jocko River below Tabor Feeder	IIF / MEF / TIF	1989 - P
513000	North Fork Jocko River below Tabor Feeder	IIF / MEF / TIF	1986 - P
513150	Jocko River below Upper S Canal	IIF/MEF / TIF	2009 - P
514300	Big Knife Creek below Upper S Canal	IIF / MEF / TIF	1985 - P
514900	Jocko River below K Canal	IIF / MEF / TIF	1986 - P
516500	East Finley Creek below Upper N Canal	IIF / MEF / TIF	1982 – P
516700	Agency Creek above Upper S Canal	Stream	1999 - P
516900	Agency Creek below Upper J Canal	IIF / MEF / TIF	1992 - P
517500	Finley Creek below E Canal	IIF	1989 – P
517800	Finley Creek near mouth	IIF / MEF / TIF	1985 – P
518000	Jocko River below lower S Canal	IIF / MEF / TIF	1989 – P
518700	Jocko Spring Creek near mouth	Stream	1993 - P
519200	Valley Creek near mouth	Stream	1993 – P
519400	Jocko River below lower J Canal	IIF / MEF / TIF	1989 – P
519500	Jocko River near mouth	IIF	2009 – P
313100	Little Bitterroot River below Camas A Canal	IIF / MEF / TIF	1982 – P
319800	Little Bitterroot River near mouth	Stream	1987 – P
164000	Dayton Creek near mouth	Stream	1992 - P
006000	Hellroaring Creek above reservoir	Stream	1982 – P
356800	Mud Creek below Ronan B Canal	IIF / MEF / TIF	1989 – P
351200	North Crow Creek at campground	Stream	1982 – P
351500	North Crow Creek below Pablo Feeder Canal	IIF / MEF / TIF	1987 – P
351900	Middle Crow Creek below Pablo Feeder Canal	IIF / MEF / TIF	1987 – P
352200	South Crow Creek below Pablo Feeder Canal	IIF	1987 - P
353000	South Crow Creek below South Crow Feeder Canal	IIF / MEF / TIF	1989 – P
354000	Crow Creek below Crow Pump	IIF / MEF / TIF	1989 – P
357100	Mud Creek above Crow Reservoir	Stream	2014 - P
359500	Crow Creek below Moiese A Canal	IIF / MEF / TIF	1982 – P
486000	Post Creek above McDonald Reservoir	Stream	1990 - P
486700	Post Creek above Pablo Feeder Canal	MEF / TIF	1992 - P
487055	Marsh Creek above Kicking Horse Feeder Canal	IIF / MEF	2001 – P
487000	Post Creek below Kicking Horse Feeder Canal	IIF	1989 – P
487600	Post Creek below F Canal	IIF / MEF / TIF	1982 – P
481500	Mission Creek below Mission A Canal	IIF / MEF / TIF	1987 – P
483000	Mission Creek below C Canal	IIF	1991 - P
483100	Mission Creek at St Ignatius	IIF / MEF / TIF	2014 – P
489500	Mission Creek at National Bison Range	Stream	1982 - P

12381400	South Fork Jocko River near mouth	Stream	1982 – P
12377150	Mission Creek above Reservoir	Stream	1982 – P
12375900	South Crow Creek near Ronan	Stream	1982 – P
12374250	Mill Creek above Bassoo Creek	Stream	1982 – P
12372000	Flathead River near Polson	Stream	1908 – P
12388700	Flathead River near Perma	Stream	1982 - P

Table S.1b: Active CSKT canal gages [RDA = river diversion allowance monitoring location, Canal headworks = canal monitoring location not assigned to RDA's; Canal operations = canal monitoring location on canal, not associated with a headworks]

Station Identifier	er Station Name Station Type		Period of Record	
510100	Placid Canal above Black Lake	RDA	1992 – P	
510510	Tabor Feeder Canal below Middle Fork Jocko	RDA	1992 – P	
510520	Tabor Feeder Canal below North Fork Jocko	RDA	1992 – P	
510570	Tabor Feeder Canal below Twin Lakes	RDA	1994 – P	
513100	Upper S Canal near headworks	RDA	1992 – P	
514000	Jocko K Canal near headworks	RDA	1992 – P	
514090	Jocko K Canal below Lamoose Creek	Canal operations	2015 – P	
311100	Camas A Canal near headworks	RDA	1982 – P	
317610	Camas B Canal near headworks	Canal headworks	2015 – P	
317710	Camas C Canal near headworks	Canal headworks	2015 – P	
482900	Mission F Canal at headworks	RDA	1994 – P	
482810	Mission DA Canal near headworks	RDA	1992 – P	
481410	Mission A Canal below Mission Reservoir	RDA	1992 - P	
482910	Mission C Canal near headworks	RDA	1992 – P	
487510	Post F Canal near headworks	RDA	1992 – P	
486920	Kicking Horse Feeder Canal above KH Reservoir	RDA	1994 – P	
352900	South Crow Feeder near headworks	RDA	1992 – P	
486800	Pablo Feeder Canal below Post Creek	RDA	1994 - P	
486830	Pablo Feeder Canal below North Crow Creek	RDA	1992 – P	
486880	Pablo Feeder Canal above Pablo Drop	RDA	1994 – P	
486891	Pablo A Canal below Pablo Reservoir	RDA	1994 – P	
486897	Pablo A Canal at Round Butte Weir	Canal operations	1994 – P	
358500	Moiese A Canal at headworks	RDA	1992 – P	
487590	Post F Canal above Hillside Reservoir	Canal operations	1994 – P	
489000	Hillside Ditch near headworks	RDA	2015 – P	
489200	Dublin Gulch in Bison Range	Wasteway	2015 – P	
489700	Coleman Coulee near mouth	Wasteway	1990 - P	
358590	Moiese MA Canal above mouth	Wasteway	1994 - P	

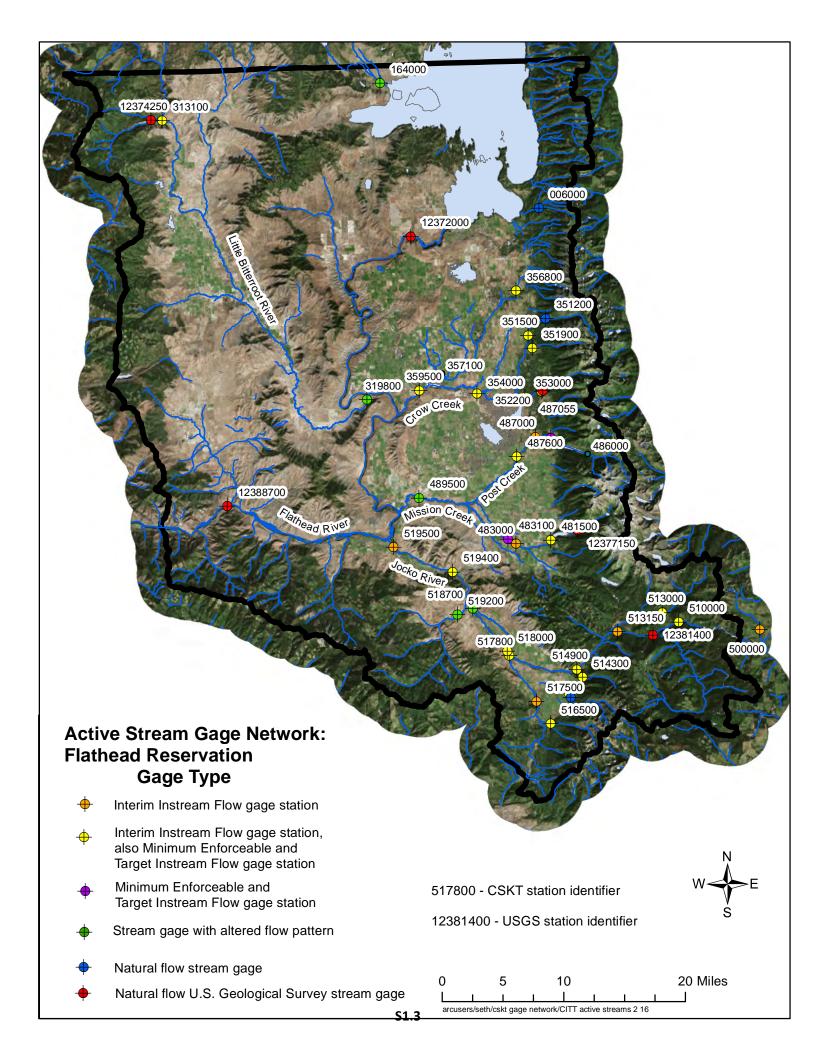

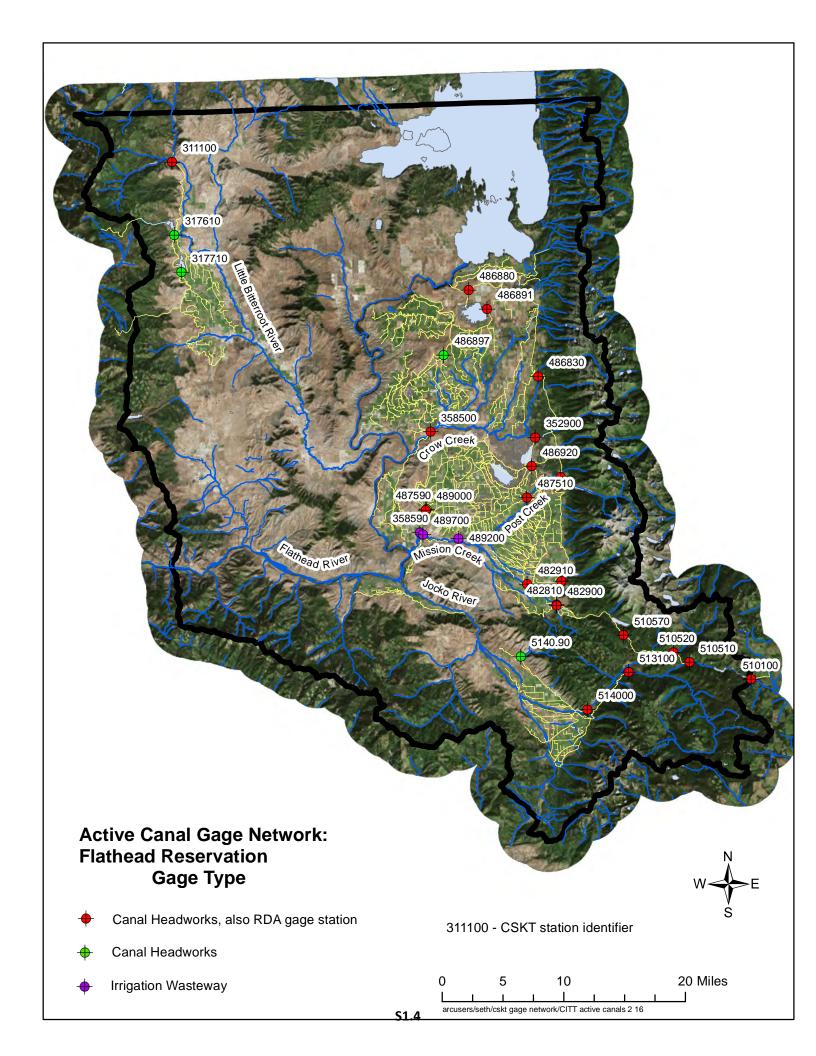


Table S.2a: New installation - Instream flow and RDA stations proposed for stilling well, equipment house, and telemetric equipment installation. Count = 18

Station Identifier	Station Name	Station Type	Period of Record	
	Revais Creek below the Revais R Canal	MEF / TIF		
513200	Upper Jocko S Canal below Big Knife Creek	RDA	1992 - 2005	
516750	Upper Jocko S Canal below Agency Creek	RDA	1993 - 2005	
516710	Upper Jocko J Canal below headworks below Agency Creek	RDA	1992 - 2005	
	Jocko E Canal below Agency Creek	RDA		
516910	Jocko E Canal below Finley Creek	RDA	1992 - 2005	
516200	Jocko N Canal below headworks below East Finley Creek	RDA	1992 - 1993	
517950	Lower Jocko S Canal below headworks below Jocko River	RDA	1992 - 1994	
519350	Lower Jocko J Canal below headworks below Jocko River	RDA	1992 - 1998	
541000	Revais R Canal below headworks below Revais Creek	RDA	1993 – 1995	
486810	Pablo Feeder Canal below South Crow Creek	RDA	1994 - 2005	
482710	Mission B Canal below headworks below Mission Creek	RDA	1992 - 2005	
483150	Mission 6C Canal below headworks below Mission Creek	RDA	1992 - 2005	
482950	Mission H Canal below headworks below Mission Creek	RDA	1992 - 2005	
356710	Ronan B Canal below headworks below Mud Creek	RDA	1992 - 2006	
006600	Twin Feeder Canal below Centipede Creek	RDA	1987 – 1988	
317100	McGinnis Diversion below headworks	RDA	1982 - 1987	
	Alder Diversion near headworks	RDA		

Table S.2b: Upgrade equipment – Active instream flow and RDA stations proposed for equipment upgrade to support telemetry. Count = 10

Station Identifier	Station Name	Station Type	Period of Record
514300	Big Knife Creek below Upper S Canal	IIF /MEF / TIF	1992 – P
516900	Agency Creek below Upper J Canal	IIF / MEF/ TIF	1992 – P
516500	East Fork Finley Creek below N Canal	IIF / MEF / TIF	1992 - P
518000	Jocko River below lower S Canal	IIF / MEF / TIF	1992 - P
510510	Tabor Feeder Canal at headworks at MF Jocko	RDA	1992 – P
482810	Mission DA Canal below DC pool	RDA	1992 - P
351900	Middle Crow Creek below Pablo Feeder Canal	IIF / MEF/ TIF	1987 - P
356800	Mud Creek below Ronan B Canal	IIF / MEF / TIF	1992 - P
482900	Mission F Canal at headworks	RDA	1994 - P
352900	South Crow Feeder Canal at headworks	RDA	1992 - P

Table S.2c: MEF and RDA locations that are proposed for a compliance monitoring protocol – staff gage or pumping plant records. Count = 19

Station Identifier	Station Name	Station Type	Period of Record	
482400	DC-2 Lateral at Dry Creek Lining	RDA	1987 - 1988	
	Falls Creek below Tabor Feeder Canal	MEF/ TIF	1912 - 1916	
	S-14 Creek below Tabor Feeder Canal	MEF/ TIF		
513150	Jocko River below Upper S Canal	IIF / MEF / TIF	2009 - р	
	Gold Creek below Upper S Canal	MEF		
	Cold Creek below Upper S Canal	MEF		
	Schley Creek below Doney Ditch	MEF / TIF		
	Doney Ditch below Schley Creek	RDA		
	Cold Creek Ditch at headworks	RDA		
487055	Marsh Creek below Marsh Creek Feeder Canal	MEF/TIF	2001 - P	
354010	Crow Pump Canal below Crow Pump	RDA	1994 - 1998	
486820	Pablo Feeder Canal below Middle Crow Creek	RDA	1987 - 1988	
	Hellroaring Creek below Twin Feeder Canal	MEF		
006500	Twin Feeder Canal at headworks	RDA	1982 - 1987	
	Twin Feeder Canal at Bisson Creek	RDA		
	Flathead Pumping Plant	RDA		
	Little Bitterroot River below Camas A Canal, above	MEF		
	Mill Creek			
	Mill Creek below Camas A Canal	MEF		
317000	Hot Springs Creek below Camas C Canal	MEF	1989 - 1997	
	Little Bitterroot River below Hot Springs Creek	No action		

Table S.2d: RDA locations that are proposed for an artificial control structure. Count = 16

Station Identifier	Station Name	Station Type	Period of Record
513200	Upper Jocko S Canal at Big Knife Creek	RDA	1992 - 2005
516750	Upper Jocko S Canal at Agency Creek	RDA	1993 - 2005
516710	Upper Jocko J Canal at headworks at Agency Cr.	RDA	1992 - 2005
	Jocko E Canal at Agency Creek	RDA	
516910	Jocko E Canal at Finley Creek	RDA	1992 - 2005
516200	Jocko N Canal at headworks at East Finley Creek	RDA	1992 - 1993
517950	Lower Jocko S Canal at headworks at Jocko River	RDA	1992 - 1994
519350	Lower Jocko J Canal at headworks at Jocko River	RDA	1992 - 1998
541000	Revais R Canal at headworks at Revais Creek	RDA	1993 – 1995
482710	Mission B Canal at headworks at Mission Creek	RDA	1992 - 2005
483150	Mission 6C Canal at headworks at Mission Creek	RDA	1992 - 2005
482950	Mission H Canal at headworks at Mission Creek	RDA	1992 - 2005
356710	Ronan B Canal at headworks at Mud Creek	RDA	1992 - 2006
006600	Twin Feeder Canal at Centipede Creek	RDA	1987 – 1988
317100	McGinnis Diversion below headworks	RDA	1982 - 1987
	Alder Diversion near headworks		

Table S.2e: Natural flow and irrigation return flow stations proposed for new installation or upgrade. Count for upgrade = 2; Count for new installation = 3

Station Identifier	Station Name	Measurement plan	Station Type	Period of Record
516700	Agency Creek above	Upgrade telemetry	Natural	1999 - P
	Upper S Canal			
351200	North Crow Creek	Upgrade telemetry	Natural	1982 - P
	West Miller Coulee	New installation	Return flow	
	Hopkins Draw	New installation	Return flow	
	Westphal Coulee	New installation	Return flow	

